LEGEND

WORK ZONE

DETOUR ROUTE

Ⓐ W06-1 22"X22"

Ⓑ W06-1 22"X22"

Ⓒ W06-2L 22"X22"

Ⓓ W06-2R 22"X22"

Ⓔ END DETOUR M04-6A 24"X36"

Ⓕ DETOUR M04-6 24"X22"

Ⓖ DETOUR AHEAD W20-2-A 60"X48"

Ⓗ BRIDGE OUT XX MILES AHEAD R3-3-C 60"X24"

Ⓘ DETOUR M04-9R 30"X24"

Ⓙ DETOUR M04-9L 30"X24"

Ⓚ WATERTOWN PLANK ROAD R3-3-C 60"X24" (W20)

SIGN ON PERMANENT SUPPORT

* SIGN READS "BRIDGE OUT .3 MILES AHEAD"

** SIGN READS "BRIDGE OUT .25 MILES AHEAD"

GENERAL NOTES:

THE EXACT LOCATION AND SPACING OF ALL SIGNS AND DEVICES SHALL BE ADJUSTED TO FIT FIELD CONDITIONS AS APPROVED BY THE ENGINEER.

ALL SIGNS INAPPROPRIATE TO THE STATUS OF THE CONTROL ZONE, INCLUDING PRE-EXISTING SIGNING IN THE VICINITY, SHALL BE COVERED OR REMOVED AS SPECIFIED IN THE PLANS AND/OR THE SPECIAL PROVISIONS OR AS DIRECTED BY THE ENGINEER.

"W0" AND "M0" SERIES SIGNS ARE THE SAME AS "W" AND "M" SIGNS EXCEPT THE BACKGROUND IS ORANGE.

ANY STOP SIGNS WHICH ARE REMOVED FOR A CONSTRUCTION OPERATION SHALL BE IMMEDIATELY RE-ESTABLISHED.

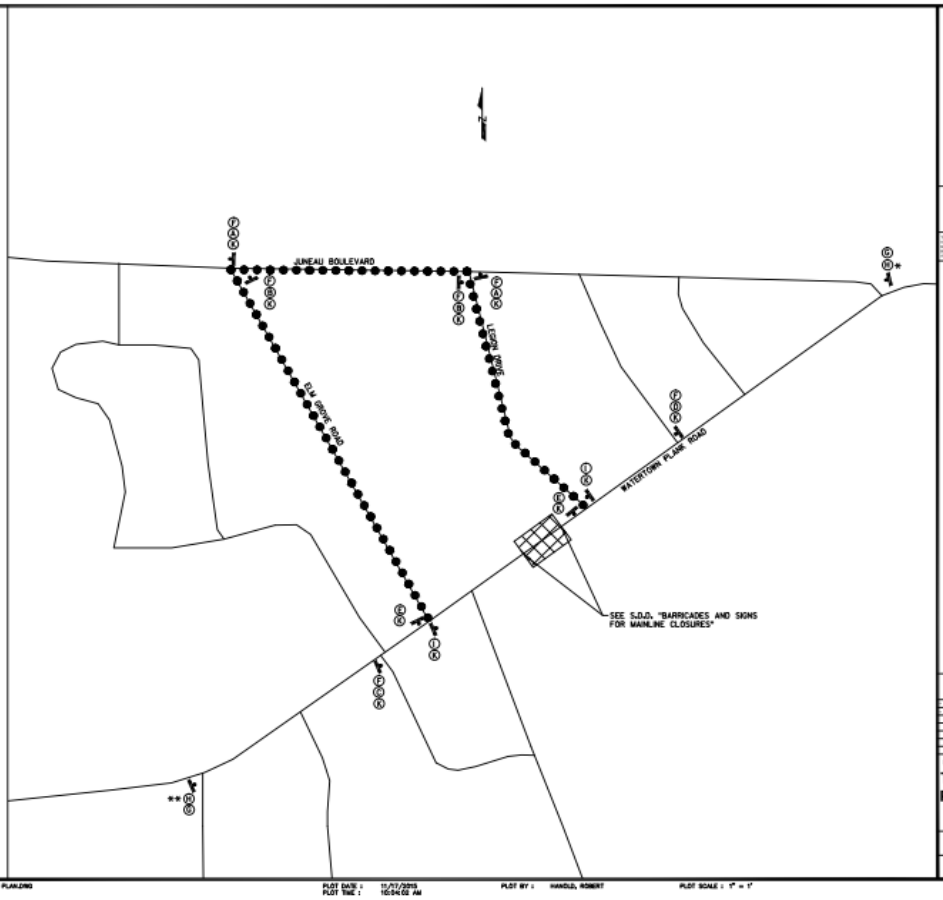

JEWELL associates engineers, inc.
Engineers - Surveyors - Architects
580 Sunrise Drive
Spring Green, WI 53588
phone: 608-588-7494
fax: 608-588-9322

THIS DOCUMENT, THE DATA AND DESIGN INFORMATION CONTAINED THEREIN, IS THE PROPERTY OF JEWELL ASSOCIATES ENGINEERS, INC. (JAE) AND MAY NOT BE COPIED, REPRODUCED, PUBLISHED, USE, SHARE WITH THIRD PARTIES OR DISCLOSED IN ANY WAY WITHOUT PRIOR WRITTEN CONSENT OF JAE. ALL RIGHTS ARE RESERVED.

Watertown Plank Road Bridge
Elm Grove, Wisconsin

Date: 11/17/2015

Date	Revision

Drawing Name: Traffic Detour Plan

Sheet No. C3.0

Project Number: E33010
